

## **Construction Update COLCHESTER Route 7/2, 2A & 127 Intersection Project – week of July 17, 2017**

Hello,

The 7-week detour on Route 7/2 in Colchester (between Creek Farm Road and Bay Road) continues in effect. Excavation of the Route 7/2 slope and installation of drainage is almost complete. The contractor expects to lay the subbase for pavement for the new road next week and begin installing curb the following week.

Traffic through the area will be controlled by a temporary signal at the junction of Routes 2A & 127 and flaggers. Even during high volume periods traffic has been following smoothly since the detour route began on June 20.


The contractor, G W Tatro, has extended their work schedule to include Saturdays, from 6 AM to 6 PM.

Access to businesses will remain OPEN at all times.



*Route 7/2 excavation near Champlain Farms gas station. Unlike the bottom of the hill where the contractor encountered deep clay soils, these soils are sandy, with good drainage. Excavation for lowering of the roadway elevation is almost complete.*

**MAP OF DETOUR ROUTE – JUNE 20 – AUGUST 4**

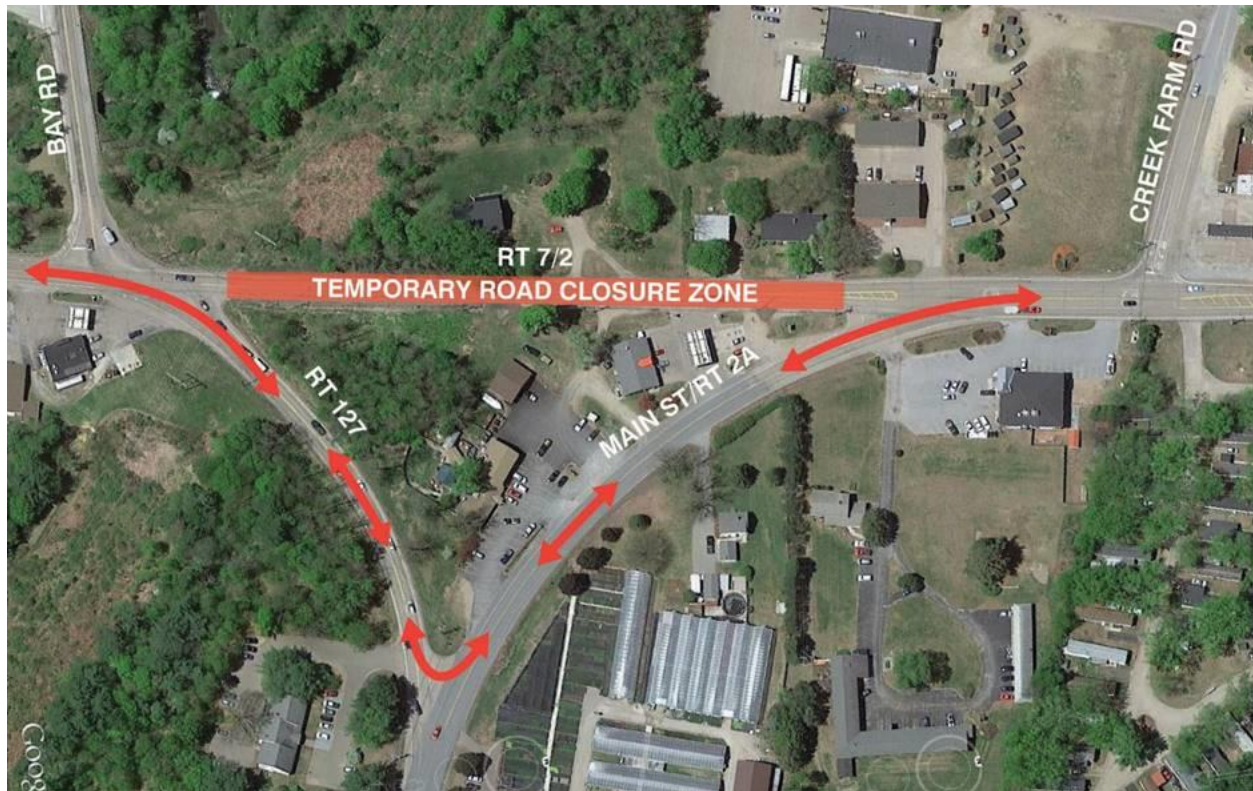

**PLEASE DRIVE WITH CAUTION THROUGH THE WORK ZONE AND "HANDS FREE" IF USING A CELL PHONE**

Best regards,

Jill

Jill Barrett  
Public Outreach Coordinator  
802.272.1248
